




Disney Two Story Modular Project
Update 1/7/22

Dear Disney Parents and the Community,

This week's dry weather allowed the contractors to complete a substantial amount of the underground utilities scope. Electrical feeders are being terminated and the new building getting prepped to be energized next week. The domestic water, storm drain, sewer, fire water and condensate lines are in and backfill completed. Fire line thrust blocks were placed with piping and backflow installation completed.

Upcoming focus the next couple weeks will be to energize the building, complete testing of all electrical and plumbing systems and start on the excavation for fencing and irrigation.

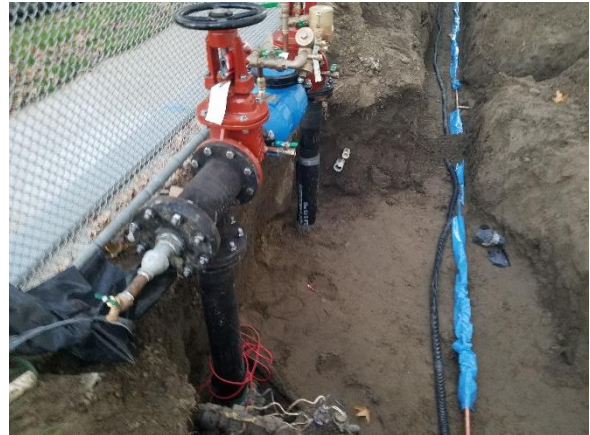

We are looking forward to the building's completion and the start of site flatwork.

Expect more exciting information coming soon!
Thank you for your support!

Larry Cross
Director of Facilities
