




Disney Two Story Modular Project
Update 10/15/21

Dear Disney Parents and the Community,

This past week, the first-floor wing wall was completed as well as the installation of low-voltage sleeves throughout the building. The lath work continued around the building, elevator tower, and elevator machine room. All 1st and 2nd level control joints, flashing, and trim, including reveals at windows and doors have been set.

Upcoming activities next week will include the start of the scratch coat application, which will last the entire week.

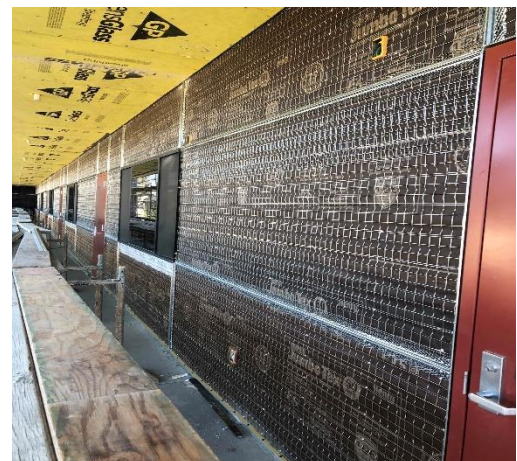

We are looking forward to the completion of the stucco scratch and finish coats and the removal of the scaffolding in the coming weeks where the building exterior will start to take shape.

Thank you for your support!

Larry Cross
Director of Facilities
