





Disney Two Story Modular Project Update 10/28/22

Dear Disney Parents and the Community,

The new blacktop playground received its first set of painted playground features Saturday October 29th. This coming Saturday, November 5th, the remaining features will be painted and any minor adjustments will be done. During the winter break, the final stages of the playground will be completed with the installation of basketball backstops, tether ball poles, a new ball wall and other features.

In the upcoming weeks we will be working on the finishing touches such as new blinds for all of the classrooms, park like seating at the lunch shelter area and other great things. The new planter wells are scheduled to be delivered on November 10th with the new trees being planted shortly after.

The pictures below are sample pictures of the new tree well planters and Crepe Myrtle 8-10' trees that will be coming very soon to the Disney!

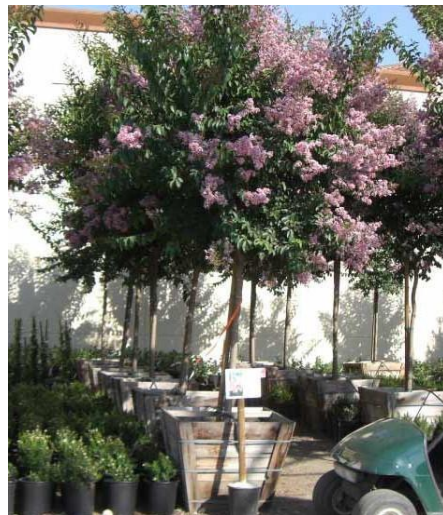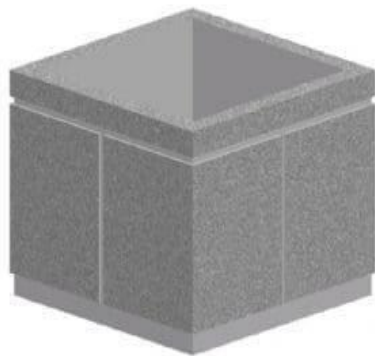

Expect more exciting information coming soon!
Thank you for your support!

Larry Cross
Director of Facilities
