



Disney Two Story Modular Project
Update 2/15/21


Dear Disney Parents and the Community,

I am happy to announce that Silver Creek is still working in full speed on the offsite building manufacturing for our Walt Disney Elementary School project.



This week they are still working on the buildup of the upper structure in some modules.

Simultaneously, they are working on the installation of framing and wall openings in the modules that already have the upper structure built.

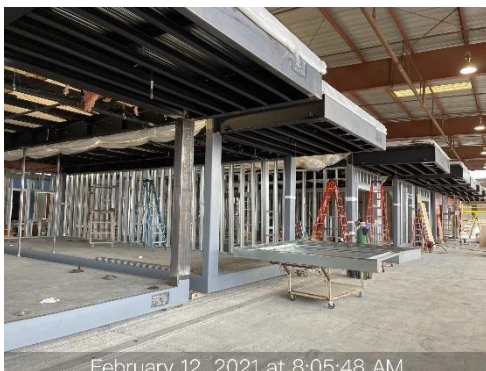

In this picture, you can see how our building manufacturing is progressing.

Additionally, Silver Creek has also started working on the closing of the walls and on the installation of doors and hardware.



Meanwhile, our bid process is underway and this week we completed two bid milestones:

1. The final list of prequalified contractors has been uploaded to our website.
2. The addendum #04 was posted to all contractors in our plan room

Site Preparations are under way with the trees being removed, playground equipment being dismantled and the temporary fencing and construction bathrooms scheduled to be put into place the week of 2/22/21.

For the week of 2/15/21 we have the very exciting bid opening on 2/18 in the early afternoon!

More information coming soon!
As always, Thank you for your support!

Larry Cross
Director of Facilities
