




Disney Two Story Modular Project Update 2/26/21


Dear Disney Parents and the Community,

This week we bring to you the following updates:

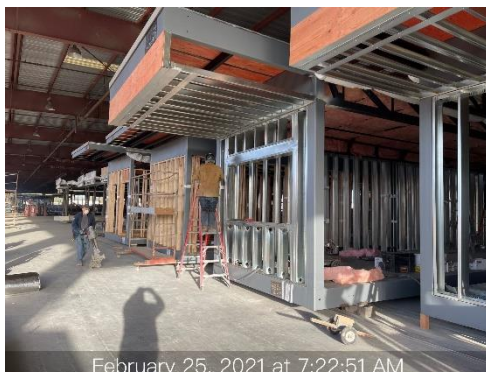

Silver Creek is still working on the framing and closure of some building modules.

Concurrently, they are working on the electrical rough-in installation.

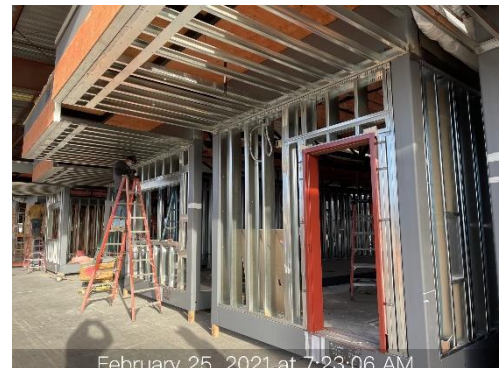

Silver Creek is also installing the building modules insulation, which is part of the building wall system.

Some of the building modules have had their window glazing installed.



Our Construction Management consultant has finished the review of the received bids. A Letter of Intent to Award was issued to all bidders, as part of the compliance to the Public Contract Code requirements, and it allows the contractors and subcontractors to start the formalities on the project. The Award Recommendation will be presented to the Board of Trustees on March 4th for approval. Soon, we will issue a Notice of Award to all approved prime contractors and once they return their signed agreements, the project will kick-start at the site.

Meanwhile, at the Disney School Site the temporary fencing has been installed and construction worker restrooms placed on site. Temporary construction power will be placed next week.

We are very excited that the beginning of our sitework is fast approaching!

More information coming soon!
As always, Thank you for your support!

Larry Cross
Director of Facilities
