



Disney Two Story Modular Project Update 2/5/21

Dear Disney Parents and the Community,


Excellent news!

I am happy to inform that Silver Creek's offsite building manufacturing is in full speed.



This week they are still working on the buildup of the floors structure for the placement of the lightweight concrete in some of the building modules.

At the same time, they are working on placing the concrete on the structures that were finalized along the week.

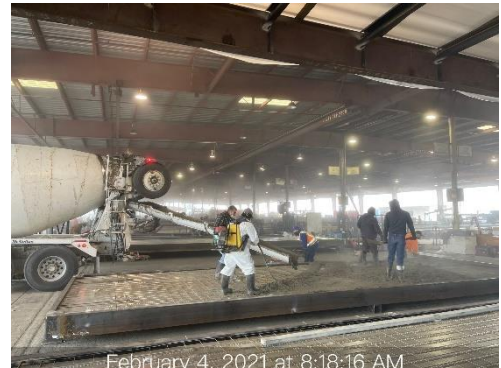

In addition, Silver Creek has also started on the welding and set up of the upper structure, which will support the second floor, on the modules that have the concrete floors already in place.

Meanwhile, our bid process is underway and this week we completed two bid milestones:

1. The prequalification process for the contractors that want to bid on Disney Elementary School project ended on 2/1/21. The list of prequalified contractors can be seen in our website.
2. The time for contractors to request for information (RFI) on the project documents ended on 2/2/21. Now, our Construction Manager is processing the RFIs and incorporating the changes and additional information on the final bid documents. A final addendum will be issued next week.

What's next ? We are looking forward to our bid opening on February 18, 2021!

More information coming soon!

As always, Thank you for your support!

Larry Cross
Director of Facilities
