



## Disney Two Story Modular Project Update 3/19/21

Dear Disney Parents and the Community,


We have enthusiastic news this week. Silver Creek has completed 90% of the offsite manufacturing of the modular building sections. The manufacturer is currently working on the restroom modules. Once these two sections are finished, the building will be complete.

Below you can see some details of the interior of one of the restrooms, the computer lab, and the group instruction room.



This image shows the installation of epoxy flooring at one of the restrooms. All of the restrooms will have the same type of flooring when they are complete.

This picture shows one of the sides of the computer lab along with partially completed ceiling. The casework seen in this room will also be installed in all of the classrooms.

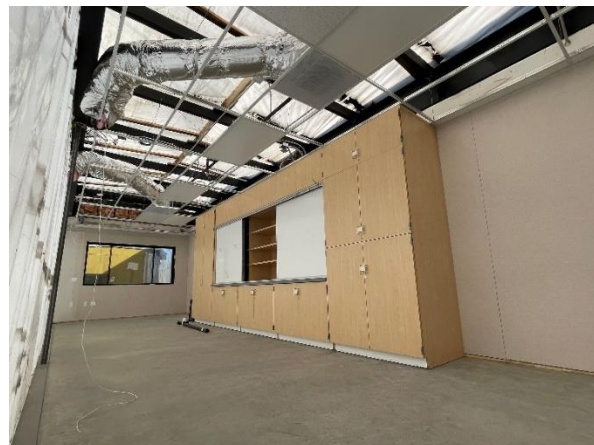



This picture shows one of the sides of the group instruction room. Here you can see the HVAC equipment, electrical panel, and overhead installation of HVAC ductwork, electrical conduits, and fire sprinklers.

In the meantime, the construction preparation phase continues, and the project is moving forward. While there may not be much site progress that is immediately visible, administrative tasks, material procurement, survey and other investigative/preparatory tasks are ongoing. These activities precede the actual start of the excavation and physical site work.

We look forward to the successful completion of the Two-Story Modular Project and providing the students of Walt Disney Elementary School with these new and innovative classrooms!

More information coming soon!  
Thank you for your support!

Larry Cross  
Director of Facilities
