



Disney Two Story Modular Project Update 3/5/21

Dear Disney Parents and the Community,


We are very excited to bring to you the following updates:

Silver Creek is moving along with the offsite manufacturing of the modular building sections and is approximately 70% complete. Many of the modular building sections have been wrapped and moved to storage. The remaining portion of the work on the stored modular sections will be completed after they have been placed and assembled on site.



Silver Creek is still working on the framing and closure of some building modules.

Here we have the module units stored at Silver Creek's yard. Those units are ready to be delivered and will be delivered once the foundation is complete at the jobsite.

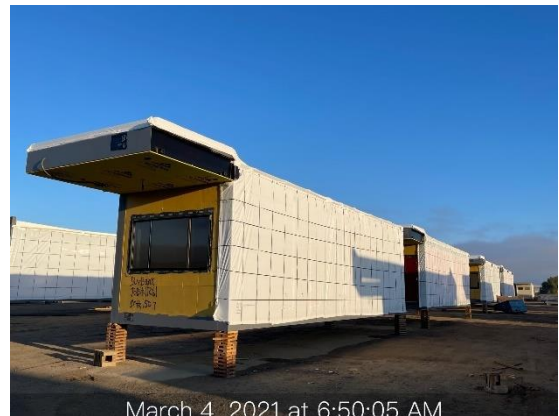

Last night, the Board of Education has awarded the contractors that will perform the site work and today our Construction Management consultant will send the Letters of Award to the approved contractors. A pre-construction meeting will be held next week with the awarded contractors and the construction will start on Monday, March 15th.

At Disney the site preparations are almost complete with just the temporary power pole and play equipment dismantling left to complete next week.

We are very excited that the beginning of the sitework is only a week or two away!!

More information coming soon!

As always, Thank you for your support!

Larry Cross
Director of Facilities
