




## Disney Two Story Modular Project Update 4/15/22

Dear Disney Parents and the Community,

This week Sunrise Telecom continued with their cable runs for the building communication and data system on the second floor. Meanwhile, Silver Creek continued the overhead work with the installation of power to the teachers' working station and installation of the fire alarm for the pull stations in the first and second floors wing wall. In addition, Silver Creek installed the elevator landing threshold on the second floor.

Focus for the next couple weeks will be completing the ceiling tiles, testing and inspection of phase 1 irrigation piping, water supply chlorination, and certification, temporary DG access for building occupancy, FA programming and testing, close-up of the building, and air balance of the HVAC system.

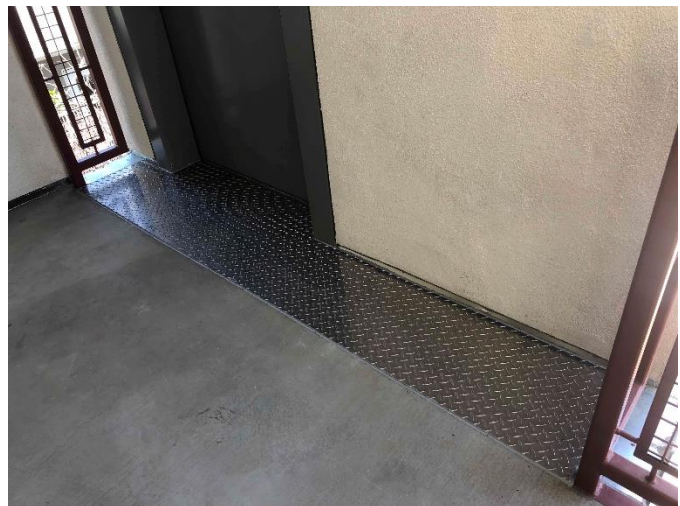

Expect more exciting information coming soon!  
Thank you for your support!

Larry Cross  
Director of Facilities
