



Disney Two Story Modular Project
Update 4/16/21


Dear Disney Parents and the Community,

This week we had our Disney Elementary School Project Groundbreaking Ceremony. The ceremony was streamed live, and we hope you were able to join us and witness this important moment in our school history.



In the meantime, the site work is in progress and Chalmers Construction Services continues with the site demolition of asphalt paving, playground equipment footings, ball wall, and other site elements.

In addition, Chalmers has also started the over-excavation work of the building area in preparation for the foundation work.

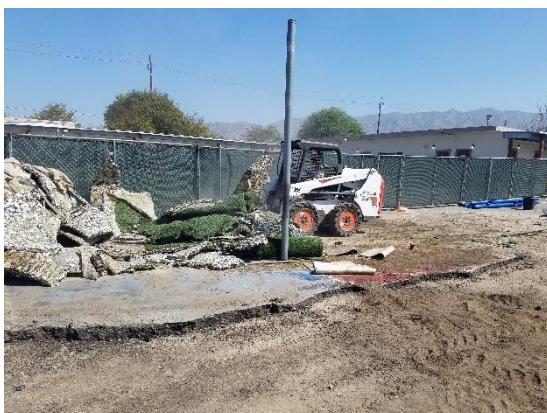



We look forward to successfully delivering the Two-Story Modular Project to the community and providing the students at Walt Disney Elementary School with this new and innovative classroom building!

Expect more exciting information coming soon!
Thank you for your support!

Larry Cross
Director of Facilities
